Salty Padel Project Proposal

Project Overview:

This project is about providing a website for Salty Padel, a limited company that hosts padel tournaments across the Southwest of England; it's run and owned by Mr. Phil Salter. Phil has asked for a website that focuses on promoting Salty Padel's events, social medias, and community.

Project scope:

We were given the following functional requirements:

- Must adapt to all platforms (it's expected that most people will view the website on phone though).
- Provide information on upcoming events (photo, location, time, date) and past events (photo, name, date).
- The website should allow photos on "who we are" and "what we do" pages.
- A section for Salty Padel's partners (the companies who permanently sponsor SP) - VX3 (clothing), The Padel Directory (directory membership), and Express Padel (padel suppliers).
- Website must be editable. Phil does not have technical programming knowledge, so we must make the website editable for him using drag-drop, upload buttons, etc.

We were also given some specifications as to what not to include in the website:

- Do not include a shop. This decision was made a few sprints in as it was eventually seen as unnecessary. Any current Salty Padel merch is handled by VX3 and there will be a link on the website that send the user to that website.
- No login/account creation system is needed for general users – this is purely down to it being unnecessary, there is nothing the website will offer if you log in. Phil will have an admin login to be able to edit the website.
- No accessible or language settings are required.
- No need to mention sponsors (other than partners) as they will change every competition.
- Do not show prices anywhere on the website, this is not the function of this website. Prices will be shown on the relevant third-part websites (like VX3 and Ticket Tailor).

Project objectives:

At minimum, this project will highlight Salty Padel's Instagram and WhatsApp, show future and past events, have who we are and what we do pages, and show SP's partners. The edit feature may only include the ability to show different future and past events and add or remove partners. There would need to be some major obstacles if this is all that was done.

If things go to plan, we hope to be able to present Phil with a fully functional and secure Salty Padel website that completes all functional requirements and highlights the SP community. It'll have a clean and modern base design (due to a container-based design); and we would like to push how far

we can take the website editing functionality: being able to change events, partners, and information is one thing, but can we also allow a way for photos, background colour, or even the logo to be changed? We would like to include as much editability as possible.

Stakeholders:

Stakeholders are people who have a vested interest, or stake, in the decision making or activities of a business (Barney, 2023, para. 1); while Phil runs Salty Padel independently, there are a few others who can be considered:

Internal stakeholder:

- Philip Salter – Salty Padel company director.

External stakeholders:

- University of Plymouth, group 4 (Willow Senior, Masa Milicevic, Beulah Oniasanmi, Carla Grigoroiu) - website development team.
- Salty Padel partners (VX3, Express Padel, and The Padel Directory) - clothing supplier, padel supplier, and directory membership supplier respectively.

Project team:

- Willow Senior: team leader. As well as general development duties, holds main communication with client, plans and facilitates (team and client) meetings, and ensures everyone is comfortable with the workload. Additionally, is happy to do a lot of documentation.
- Masa Milicevic: developer. Asked to focus on backend JavaScript over frontend duties but will still contribute to frontend visuals.
- Beulah Oniasanmi: general developer. Flexible; can work on any part of the website. Assisted with Carla's designs by designing the login page.
- Carla Grigoroiu: designer. As well as general development duties, created most of the design plans in the planning stage.

Timeline:

Due to bringing in an external client, group 4 started earlier than most which means our sprints don't line up exactly. In the following table and chart, the sprints will start during the week we had our initial client meeting.
Important dates and deadlines:

Sprint	Date/deadline	Description
-	22/9/25 - 29/9/25	Group 4 team formation
-	3/10/25	Bring in SaltyPadel
1	10/10/25	Initial client meeting
3	28/10/25	Begin prototype creation
6	9/1/26	Interim submission
7	16/1/26	Prototype demonstration and Q&A

14-15	27/4/26 - 5/5/26	Project handover to client
15	5/5/26	Final submission
15	6/5/26	Showcase presentation

Gantt Charts are useful for visualising the schedule and timeline of a project. It breaks down the project and shows how long each task should take and where they take place in the timeline. While it won't always be possible to stick by the chart exactly, it does give us an idea of where we're at and what more needs to be done. The following screenshot shows how my project was broken down and what the schedule for each task is. The rest of the Gantt Chart visuals can be found here: COMP2003 Gantt Chart.xlsx

			Format: MM/DD/YYYY		
	Task name	Duration	Start	End	Extra comments
1	**Salty Padel wesbite creation**	**208 days**	**10/10/2025**	**5/5/2026**	
2	**1. Design**	**41 days**	**10/10/2025**	**11/20/2025**	
3	1.0.1. Initial designs	10 days	10/10/2025	10/20/2025	
4	1.0.2. Improved designs	31 days	10/20/2025	11/20/2025	Long time between meetings due to other assessments
5	**2. Development**	**157 days**	**11/21/2025**	**4/26/2026**	
6	**2.1. Interim prototype**	**57 days**	**11/21/2025**	**1/16/2026**	**Unless mentioned otherwise, all of this is frontend**
7	2.1.1. Backend Single Page Application	2 days	11/28/2025	11/29/2025	
8	2.1.2. Home page	30 days	11/29/2025	12/28/2025	Due to other assessments, this took a long time - future pages will be faster
9	2.1.3. Who we are page	1 day	1/2/2026	1/2/2026	
10	2.1.4. What we do page	1 day	1/4/2026	1/4/2026	
11	2.1.5. Past events page	1 day	1/2/2026	1/2/2026	
12	2.1.6. Upcoming events page	1 day	1/4/2026	1/4/2026	
13	2.1.7. Admin login	1 day	1/2/2026	1/2/2026	
14	2.1.8. Admin home page	1 day	1/6/2026	1/6/2026	
15	2.1.9. Admin past events page	1 day	1/7/2026	1/7/2026	
16	2.1.10. Admin upcoming events page	1 day	1/7/2026	1/7/2026	
18	**2.2. Final website**	**100 days**	**1/17/2026**	**4/26/2026**	**Will involve more backend, but don't officially restart until 26/1/26**
17	2.1.11. Backend grid function	2 days	1/17/2026	2/17/2026	
19	2.2.1. Add in "quick additions"	1 day	1/19/2026	1/19/2026	Social media, event, and shop hyperlink buttons,
20	2.2.2. Add local database	15 days	2/1/2026	2/15/2026	For admin login details
21	2.2.3. Add admin login function	13 days	2/17/2026	3/1/2026	
22	2.2.4. Admin edit functionality	35 days	3/3/2026	4/6/2026	Large task - will take a while
23	**3. Usability testing**	**38 days**	**3/20/2026**	**4/26/2026**	**Testing will be done all throughout development, but usability testing will be saved until the end**
24	3.0.1. Usability testing	36 days	3/20/2026	4/24/2026	Testing will be repeated after any big changes, so I will span it across the given time
25	3.0.2. Fix bugs	34 days	3/24/2026	4/26/2026	Similarly, bug fixing will be done all throughout usability testing
26	3.0.3. Final changes	16 days	3/31/2026	4/15/2026	We will stop accepting any big change in the weeks before handover to ensure everything can be finished
27	**4. Handover to client**	**9 days**	**4/27/2026**	**5/5/2026**	
28	Teach client how to use website	1 day	4/28/2026	4/28/2026	
29	Ensure setup goes smoothly	4 days	4/29/2026	5/2/2026	

Research:

As the name suggests, Salty Padel is about the sport padel. It's a racquet sport that uses similar scoring to tennis but is played on smaller courts enclosed in glass which players can bounce balls off (Jones, 2024, sect. 3). Padel is still a relatively new sport which means there isn't a huge amount of padel competitions; however, when designing our website, Phil gave us two examples to look at: AccessPadel and GoldenPadel.

Phil has shown preference to AccessPadel's design, its dynamic design is visually appealing and less cluttered than the GoldenPadel site. While GP is strictly a merchandising company, AP highlights its community and services; the website itself isn't laid out well (too much whitespace and text clipping into photos), but its content is excellent and something SaltyPadel wants to present themselves.

What sets SaltyPadel apart is that it offers everything its competitors offer under one brand – SP has a very large community (a WhatsApp group of over 400 people) which Phil would like to emphasise, as well as selling merchandise such as rackets and clothing (see appendix for shop link).

Assuming we're using AccessPadel as design inspiration, the website will need a good mixture of whitespace, event photos, and information. Community is built on trust, inclusivity, and fostering a

sense of belonging (Celestine, 2016, sect. 1), characteristics that SaltyPadel represent on and off the courts, so the website should be user-friendly and show off what being part of the community means.

Proposed solution:

For SaltyPadel's website, we propose a website that focuses on community over merchandise; it should feature community/event photos, testimonials, and allow people to learn more about belonging in a community like SP. Users can join the SP WhatsApp, view past and upcoming events, learn more about Phil and the formation of SP, or head over to the external merchandise website.

The website will be designed to be dynamic (information fades into view as you scroll down) and feature colours commonly used in SP social medias (#F0FF70, #FFF9FC, etc.); the different colours, photos, and text will remove large amounts of unappealing whitespace. SP (currently) has three partnered companies, their logos will be displayed on the website, as well as any social media logos Phil would like to advertise.

As Phil doesn't have technical knowledge around web development, we will design the website to include an admin login where he can edit text, images, and events. The exact scope of how far we can take this editing feature is currently uncertain, but we will give him as much creative freedom as possible.

This website will act as an advertisement for SaltyPadel community, events, and merch; it will then direct the user to external resources. For example, the website will advertise the community in hopes that people will join the WhatsApp via the join link. Actions like buying merch or event tickets will not take place on this website.

Use of AI:

Use of AI is required in this assignment and we already have a few plans of how to use it. Each of us will use AI differently (e.g., Carla uses it to help her summarise information for when she creates her documents), so the exact usage will vary a little, but it may be used for guidance for complex code or to help summarise new research topics.

The most notable place AI will help is with debugging; debugging is notorious for being slow and tedious, but AI can quickly spot and explain bugs in codes: what code is broken, why it's broken, and what could be done to fix it. Using AI here will speed up debugging significantly and give more time to the rest of the project.

LSEP:

This section will cover any LSEP (legal, social, ethical, and professional) considerations in SaltyPadel and the website, it will also cover sustainability and community involvement. Some points may cover more than one section; these will be pointed out as we go through.

Starting with legal considerations, despite not gathering any user data, cyber security is still essential to the website. A local database is used to store the admin's credentials which means it must be kept encrypted and programmed in a way that stops SQL injections (such as parameterised queries).

All information on the website (times, dates, event details, etc.) should be kept accurate under the Consumer Protection Law.
Trademark protects company brands while copyright protects the website from being stolen/edited, both of which Phil has considered but ultimately decided against for now. SaltyPadel is still a young company, and it's thought that a trademark or copyright wouldn't give much benefit for the price it costs.
The final big legal consideration involves using photos on the website. SaltyPadel is a community-focused company and want to show this off by including community/event photos on their website, this comes with a consent factor. However, Phil has automatic consent to use any photos taken from the events when participants sign the event contract; he will still double check with individuals if it's okay to use their image though.

Thinking about social considerations, we need to acknowledge that a lot depends on Phil's WhatsApp community of over 400 people. Not everyone has WhatsApp which is why Instagram is important here, it ensures the largest populace of people possible can access SaltyPadel content and news. SaltyPadel promoting their community-based events add to the local sport community more effectively than big corporate events; it's also prominent in inspiring women in padel with multiple events hosting 48 women – the most in the southwest. They were even named and praised in a blog about how well they encourage women in this sport (the link to which can be found in the appendix).

Ethical considerations must be acknowledged as they represent a company's integrity; a trusted company will get more patrons than its competitors. Multiple links on the website will lead to external apps/websites (e.g., WhatsApp and VX3), ethically and legally it's important to ensure users are made aware of this before they are sent. Unexpectedly being sent to other places is how users lose trust in a website.
The website will feature testimonials from previous competitors about their experience with SaltyPadel; it's important that these testimonials are accurate and truthful – they shouldn't be edited to make the company look better nor should they be made up. False testimonials are likely to get exposed and reflect badly on the company.

Professional considerations are generally straightforward, it's all about finding the balance between a professional and fun website. Professionalism is key for the site to be trusted by new visitors, but not too much that it loses its human touch. At the end of the day, SaltyPadel is focusing on creating a welcoming community and having fun, not about formality.

Finally, I would like to discuss sustainability – an important topic in contemporary times. During tournaments, SaltyPadel goes through a lot of balls, many of which shouldn't be used in other tournaments. Instead of letting them go to waste, the balls are donated to schools or similar facilities to have an extended life. Moreover, the creation of this website results in reduced printed material – more sustainable than using up paper and other resources for the informatics.

Work Breakdown Structure (WBS):

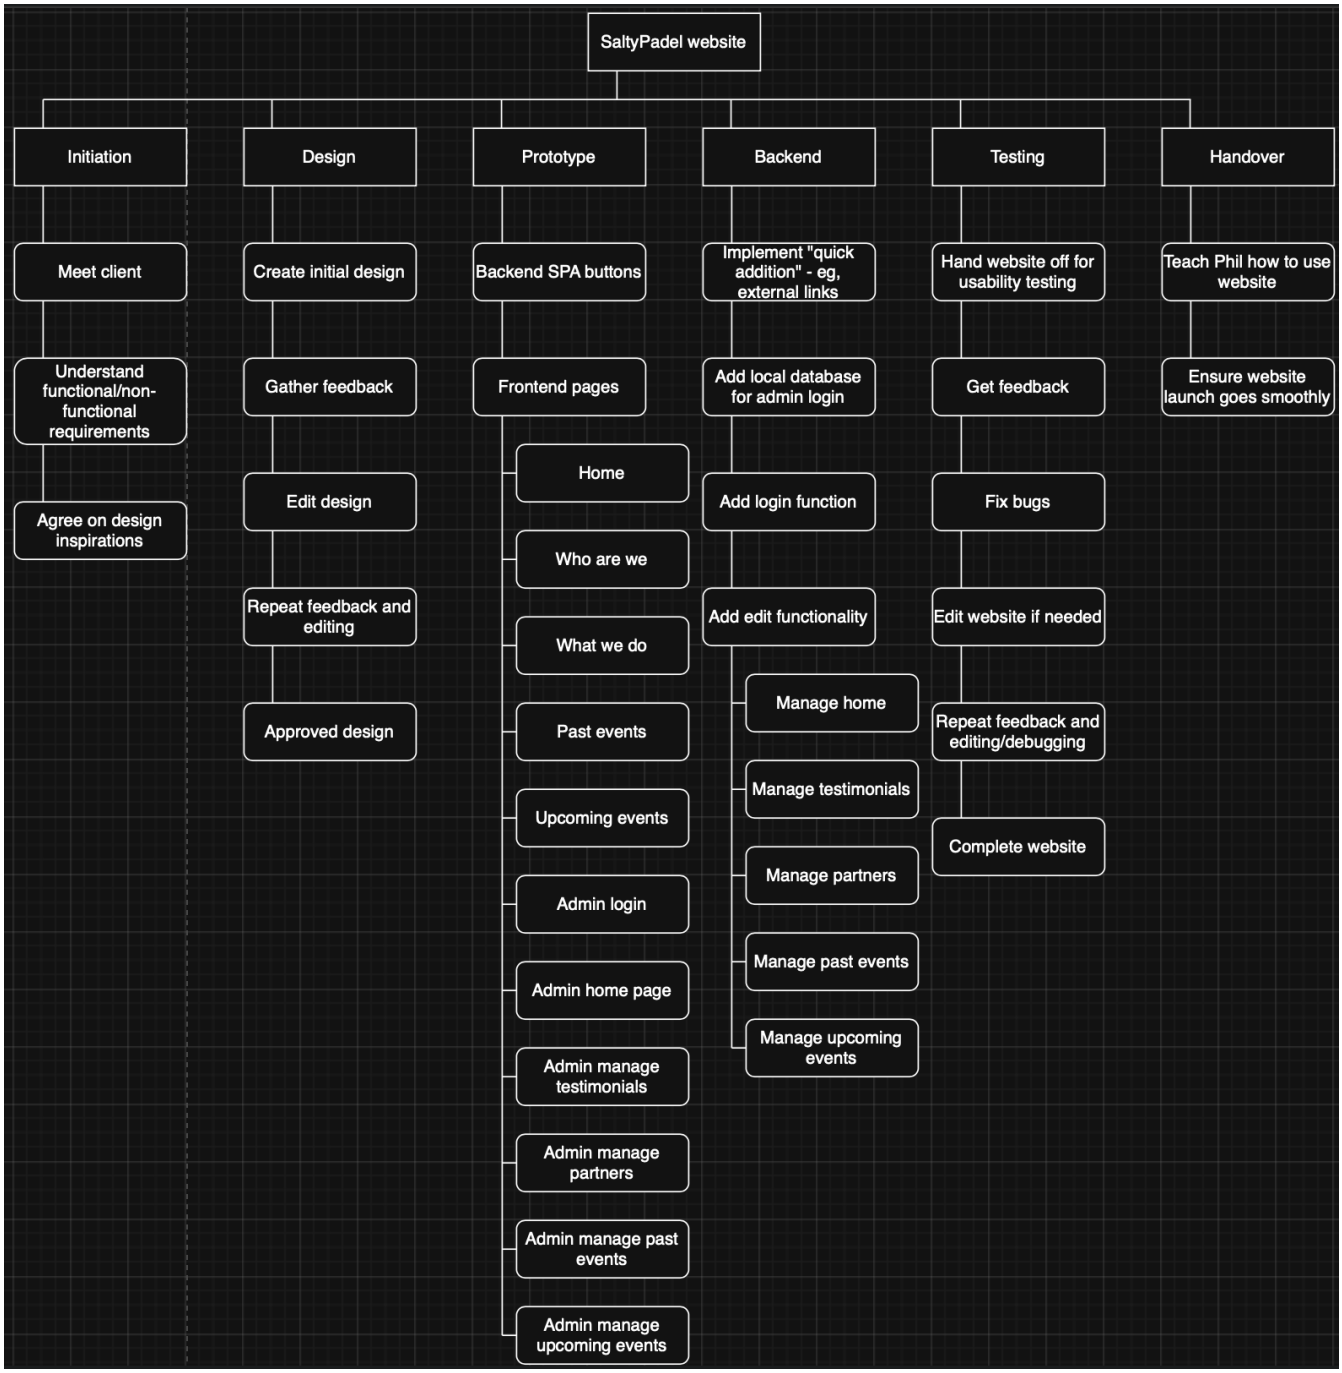

A Work Breakdown Structure (WBS) is a project management method used to assist in the implementation of large projects. It works using decomposition – breaking down complex problems into smaller, more manageable tasks – and demonstrates the steps and scope of each overarching task.

This project can be broken down into 6 big sections: initiation (meeting the client and defining functional requirements), design (designing what the website will look like and how to include the requirements), prototype (frontend visuals and SPA functionality), backend (editing features and other small bits), testing (usability testing, debugging, and tweaking), and handover (website training and deployment).

This diagram starts from the left section and goes down the list; the hierarchal order is significant, going down, each task leads to another. However, “frontend pages” and “add edit functionality”

connect a list of mini tasks, these tasks can be done in any order. This diagram acts as a guide and shows what we are working on and what comes next.

Resource plan:

I will use the WBS to identify and elaborate on tasks, it would be unproductive to speak about every mini task, so I'll go over the most important sections. I will give the section and task the resources belong to, explain my reasoning, and then list what/who exactly is needed. It's worth noting that financial considerations would usually be acknowledged here, but as this project is going for free, none are needed.

Section	Task	Resources
Initiation	-	The first section was all about meeting Phil, getting to know SaltyPadel, and understanding the project, so not many resources are needed here other than a way to facilitate first communication with Phil and the initial meeting which kicks this all off. - Tech for teams meeting - All developers + Phil
Design	Create initial design	The initial design will be done by Carla (with help from Beulah), we're confident that her creative abilities and experience with Figma will result in a clean and professional website. - Figma - Carla + Beulah
Design	Gather feedback and edit design	Most of the feedback will be done through virtual client meetings which leads to more Figma editing from Carla and Beulah. - Tech for teams meeting - Figma - All developers + Phil
Prototype	Backend SPA buttons	The Single Page Application (SPA) will be done by Willow as she has programmed this exact feature previously to good results. This needs to be done first so developers can move between pages while they're developing the visuals. - Tech for IDE - GitHub - Willow
Prototype	Frontend pages	The prototype (which will be submitted as part of the assessment) will mostly be done by Beulah and Masa as they are comfortable with the code side of development. Willow and Carla will be working on other features in the meantime but can jump in to help at any time. - Tech for IDE - GitHub - All developers (although Masa and Beulah take the lead here)
Backend	Implement quick additions and add local database	"Quick additions" mostly refers to adding accurate information or social media links given by Phil; meanwhile, the database will be in SQLite and store the login details for the admin account. It's not been decided who will do these tasks, but Willow is a likely candidate. - Tech for IDE - GitHub - Undecided developer (possibly Willow) + Phil

Backend	Login and edit functions	A substantial amount of work which will be split among all group members. Relies on database being intact first. - Tech for IDE - GitHub - All developers
Testing	Usability testing	Phil has stated he has a close group of 12ish people who would be able to help test the website. It's undecided on how exactly this will be executed, but Phil will pass back all feedback and bug reports. - Others will need access to the website (keeping in mind most won't have technical-knowledge or an IDE). - An open line of communication will be critical here to exchange instructions and feedback - Willow (to retrieve info) + Phil and his associates
Testing	Fix bugs and edit website	If feedback gives strong opinions on something needing to be changed, then the dev team will get on it, but bug fixes are the most important job to be done. Most should be quick tweaks but anything more may require more than one person. - Tech for IDE - GitHub - All developers
Handover	Teach Phil how to use the website	Will most likely be done by Willow, but could also be done through a client meeting so everyone can pitch in. - Phil will need to access the website on his own device – doesn't have technical knowledge or IDE - Willow (maybe all developers) + Phil

Risk Management:

A risk assessment was created and uploaded to the GitHub (the link to which can be found in the appendix), but I will share my assessment matrix here as well as some risk events and their scores. At the bottom of this section, I will also cover some contingency plans.

		Risk assessment matrix				
Probability	5	Medium/ High	Medium/ High	High	High	High
	4	Low/ Medium	Medium/ High	Medium/ High	High	High
	3	Low/ Medium	Low/ Medium	Medium/ High	Medium/ High	High
	2	Low	Low	Low/ Medium	Low/ Medium	Medium/ High
	1	Low	Low	Low	Low/ Medium	Medium/ High
		1	2	3	4	5
		Impact				

Risk event	Probability considerations	Prob score	Impact	Impact score	Risk score

Client drops out	-No signs of client dropping out, but must be considered	1	-It would be a morale dropper and complicate things for a while, but lecturers would pick up where client left off	3	Low
Group member drops out	-Students can't just choose not to do this work; something bigger and more unlikely would have to happen for that	1	-Workload would be spread as evenly as possible, but it's already been proven that three assessments are a lot to handle at once, so more work would be noticeable	4	Low / medium
Other assessments getting in the way of this project	-The other assessments have already proven to be a heavy workload -All assessments are due on the same date	4	-Any particularly large/long assessments may slow down production of the project -If one or more persons is held up with other assignments, their project workload may hold the others back	4	High
Project slowed due to illness	-Universities are pathogen hotspot, so illness is not uncommon	4	-It is unlikely that anyone would contract anything of great importance; it's more likely to slow progress than stop it	1	Low

Contingency plans:

- All code is to be kept on GitHub at all times, this stops accidental deletion or lost code due to technical failure.
- It has been emphasized that anyone struggling should reach out for help, whether it's with workload, mental health, or other technical issues; the group is prepared to take the pressure from that person by taking on work.
- Most documents have more than one copy, one on GitHub and one elsewhere (local storage, OneDrive, external website, etc.).
- Extenuating Circumstances can be used if we are running too short on time, it would give us an extra five days.
- We peer review each other's work when it comes up to ensure everything's been done to the correct standard and any bugs have been caught.

Communication plan:

During the project we will have biweekly sprint meetings with our group tutor who checks on what work has been done in that sprint; we will also have biweekly client meetings with Phil to show him our progression, get his thoughts/feedback, and to ensure he's happy with the direction things are going. Team meetings take place whenever one of us wants one – this could be if we feel like we have something important to share or there a piece of work we need to collaborate on (e.g., the assessment video).

Moving away from meetings, we also communicate via email and WhatsApp. Any questions aimed at lecturers happen over email; while communication with Phil happens between him and Willow on WhatsApp – she can message him any time with any questions. Communication between the group members happens through a WhatsApp group or private message if needs be.

Quality management:

The group will be reaching for the highest marks possible by producing a consistent and high-quality website for SaltyPadel. We'll do this through a few methods, starting with peer checking the work we complete. On Trello, once we complete a task, it will be moved into the "review needed" section where other group members check over the work to ensure it follows our guidelines.

Our visual guidelines come from a document made by Carla that can be found on the GitHub called the "SaltyPadel_UI_CheatSheet". All pages on the website follow a certain design structure (can be seen in the Figma in the appendix), so the cheat sheet gives global instructions on how to layout the page: it gives colour hex codes, page segment measurements, text specifications, and more. This document ensures the page design is consistent throughout the website.

Some quality management will also come from the client; during the biweekly client meetings, we walk Phil through everything we've done to keep him in the loop and to get his feedback. As the website represents Phil and his company, he will hold it to a high standard; if there's anything he's unhappy with, he can mention it, and we will fix it.

Monitoring and evaluation:

This section is about how we'll track progress of our project using key performance indicators (KPIs) and client feedback. Additionally, KPIs help with quality management by monitoring quality and consistency. The following table will name and describe our KPIs.

Name	Description
Gantt Chart	Our Gantt Chart (as spoken about earlier) helps visualise the timeline for each part of the project. Although singular tasks can vary compared to their given timeline, deadlines are concrete and must be followed. All tasks will be completed on time, and the Gantt Chart can be used as a list to understand what comes next.
Assessment submission dates	At the core of this project, it's still an assessment and there are deadlines we need to meet; these deadlines will guide what work needs to be done by what time. For example, our first deadline is the 9th of January, the project plan, LSEP, and prototype are the most important factors for this. Having this assessment ensures that this work will be done to a high standard (the other deadline is the 5th of May).
Biweekly sprint meetings	We will always have a sprint meeting with our group tutor every fortnight to track our progress. If not enough has been done, we may lose marks and will be encouraged to speed up progression.
Biweekly client meetings	In our biweekly client meetings, we will show Phil what progress has been completed and explain what will be done next. Knowing we will show our client our recent progress will be a boost to stick to the plan.

Budget:

As this project is developed for free, there are very few budget considerations that need acknowledging. Phil already has a contract for web hosting and a domain name which costs him £14/month.

Outside of web hosting, Phil may need to go up to Plymouth at some point for university-specific business. Additionally, he's invited the group to come and experience one of his tournaments, travel will likely be covered by students, but entry will be covered by Phil.

Approval process:

Approval will change depending on what the work is; anything small like approving designs can be done over message or client meetings. Anything larger, like the project proposal, may involve some kind of approval text (e.g., this page has "approval text" at the bottom which will need to be signed off by Phil).

No big decisions will be made without the development team and Phil. After approval for the project proposal is finished, the next approval needed will involve the prototype – this is a big one as it will be the (mostly) finalised design of the website. The final approval will be at the end of the project where some handover document may need to be created and designed to ensure Phil is happy with the final product.

Change management:

Our plan for project scope changes depends on how big of a change is required. Take, for example, if the client wants some big visual change, the development team would need to go back and edit our original designs to the client's specifications. Once finalised, we would then be able to change our existing programming using the UI cheat sheet (assuming the visual change isn't too great that a new cheat sheet would be made). If the project scope was something to do with backend details, say if the client decided they wanted a user database, the designs may only be tweaked to add new user pages and login page; most of the work would just be altering the local database to handle large data.

It's unlikely that any schedule changes would happen as Phil does not have a deadline for this project, but any changes that might be thrown out wouldn't be too problematic as our schedule is already flexible. An example would be client meetings, these meetings run by Phil's schedule, if something changes then the meeting will be rearranged to another suitable date.

Our project isn't planned to use many resources, the most we need is tech for IDEs and meetings, GitHub, and Teams. It's unlikely anything will happen to these resources, but if we discover what we have doesn't cover the project scope, then we will research and apply new resources.

Closure:

After development ends, the job will change to teaching Phil how to use the website, web hosting, and future maintenance. Website training should be simple enough as Phil has been able to observe development all throughout the year, this will likely revolve around the editing feature. Web hosting

requires multiple parts such as a domain name, DNS, SSL certificate (HTTPS), and the hosting itself; Phil already has a deal with a hosting company, so most of this is already set up.

Finally, future maintenance; we will build the website to the best of our abilities to avoid any future problems, but in case any do show up, Phil and Willow share a mutual friend and can stay in contact – she's willing to help with maintenance.

Client approval:

I, Philip Salter, am happy with everything that's been said in this proposal and accept the project solution given to me. I give Willow, Carla, Beulah, and Masa permission to go ahead with this project.
Signed:

Philip Salter.

References:

Barney, N. (2023). *What is a stakeholder?* TechTarget. Available at: https://www.techtarget.com/searchcio/definition/stakeholder . (Accessed on 10th December 2025).

Celestine, N (2016). *10 Characteristics: What makes a positive community.* PositivePsychology. Available at: https://positivepsychology.com/10-traits-positive-community/ . (Accessed on 2nd January 2026).

Jones, J. (2024). *The rise of padel and why it's so popular.* BBC Sport. Available at: https://www.bbc.co.uk/sport/articles/crrlnlj8lrxo . (Accessed on 12th December 2025).

Appendix:

GitHub link: https://github.com/Plymouth-University/comp2003-2025-2026-team-4 .

SaltyPadel shop link (to be incorporated into project): https://vx-3.com/collections/salty-padel .

Risk assessment link (also found on GitHub): COMP2003 Risk Assessment.docx .

Figma – SaltyPadel design: https://www.figma.com/SaltyPadel .

SaltyPadel supporting women in padel – blog: https://www.thepadeldirectory.co.uk/post/what-women-really-want-from-padel-events
